

Monthly Performance Report – June 2024

Kestrel Ridge Wind Farm (75.6 MW)

David Chen · 09 July 2024 · KR-OPS-RPT-2024-06

1. Summary


Kestrel Ridge generated **11.5 GWh** in June 2024, 3.6 % above the P50 budget of 11.1 GWh. Availability fell to **96.4 %**, below the contract target of 97.0 %. Mean hub-height wind speed of 6.8 m/s was close to the long-term mean (6.7 m/s).

The 3-month reliability run under the O&M contract was completed on 15 June with a time-based availability of 95.7 % (threshold 95.0 %). Take-over certificate signed on 19 June.

2. Production and key figures

KPI	June 2024	Budget / target	YTD 2024	YTD budget
Net generation (GWh)	11.5	11.1	41.0	42.0
Time-based availability	96.4 %	97.0 %	95.7 %	97.0 %
Capacity factor	21.1 %	20.4 %	24.8 %	–
Mean wind speed at hub height (m/s)	6.8	6.7	–	–

Source: Kestrel Ridge SCADA, revenue meter at 132 kV point of connection. Budget = P50 (2024 post-construction yield assessment).

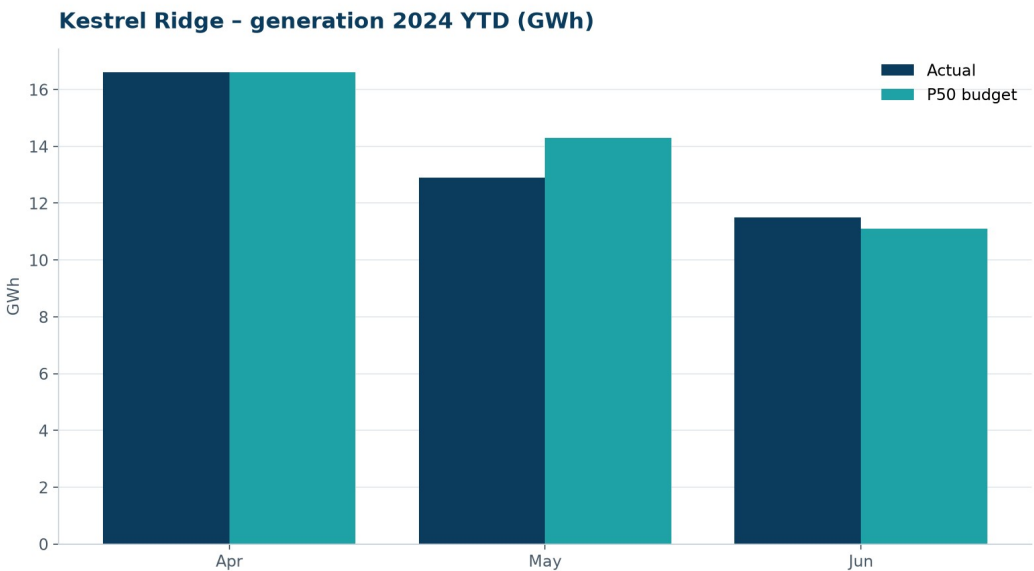

Monthly generation vs. P50 budget, 2024 year to date

3. Availability and downtime

Total turbine downtime attributable to the contractor amounted to 36 turbine-hours for the top events listed below. No grid or force majeure exclusions were claimed this month.

Turbine	Event	Downtime (h)
T-14	hydraulic oil leak at rotor brake caliper	12
T-08	service lift fault – lift locked out, turbine stopped for rescue cover	10
T-10	anemometer heater failure – sensor replaced	9
T-10	service lift fault – lift locked out, turbine stopped for rescue cover	5

Top downtime events of the month (SCADA event log, reviewed with Highline Wind Services).

4. Maintenance

- 12 corrective work orders closed, 3 still open at month end.
- Gearbox oil samples taken on six turbines as per the quarterly rota; results within limits.

5. Health, safety and environment

Indicator	Month
Hours worked on site (Highline + Weyland)	2,745
Lost time injuries	0
First aid cases	0
Near misses reported	1
Safety observations	9
Environmental incidents	0

No environmental incidents. Bird carcass searches were carried out on schedule (fortnightly, all turbines).

6. Outlook

The P50 budget for next month assumes normal seasonal wind; no planned outages beyond routine maintenance.

Prepared by Sara Lindgren (Performance Analyst); reviewed by Ben Okoye (Site Manager) and David Chen (Asset Operations Manager).
