

Monthly Performance Report – July 2024

Kestrel Ridge Wind Farm (75.6 MW)

David Chen · 09 August 2024 · KR-OPS-RPT-2024-07


1. Summary

Kestrel Ridge generated **10.3 GWh** in July 2024, 5.5 % below the P50 budget of 10.9 GWh. Availability fell to **96.9 %**, below the contract target of 97.0 %. Mean hub-height wind speed of 6.6 m/s was close to the long-term mean (6.6 m/s).

2. Production and key figures

KPI	July 2024	Budget / target	YTD 2024	YTD budget
Net generation (GWh)	10.3	10.9	51.3	52.9
Time-based availability	96.9 %	97.0 %	96.0 %	97.0 %
Capacity factor	18.3 %	19.4 %	23.2 %	–
Mean wind speed at hub height (m/s)	6.6	6.6	–	–

Source: Kestrel Ridge SCADA, revenue meter at 132 kV point of connection. Budget = P50 (2024 post-construction yield assessment).

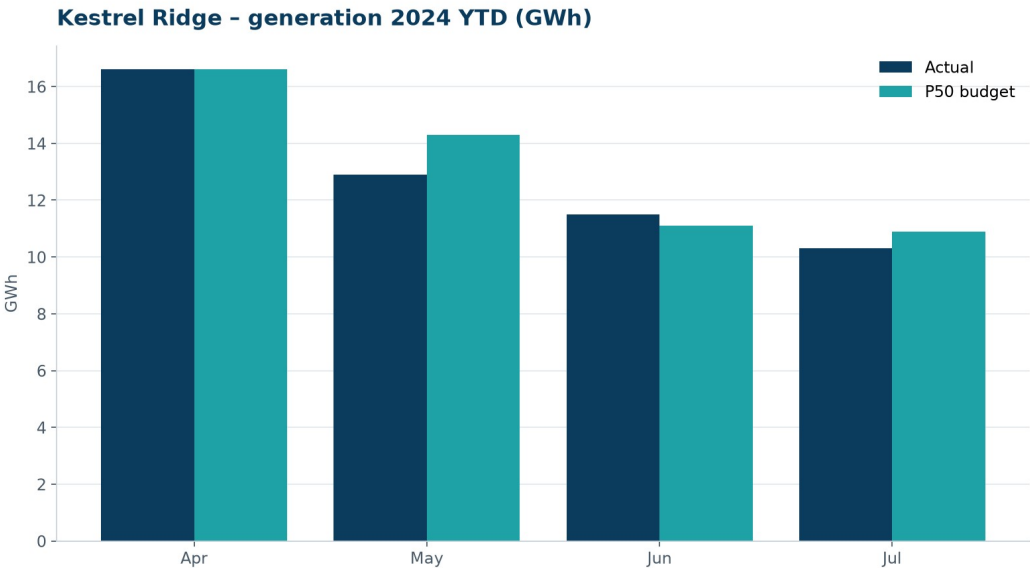

Monthly generation vs. P50 budget, 2024 year to date

3. Availability and downtime

Total turbine downtime attributable to the contractor amounted to 76 turbine-hours for the top events listed below. No grid or force majeure exclusions were claimed this month.

Turbine	Event	Downtime (h)
T-07	converter fault – IGBT module replaced	30

T-16	nacelle cooling fan motor failure	18
T-18	hydraulic oil leak at rotor brake caliper	15
T-13	hydraulic oil leak at rotor brake caliper	7
T-12	main shaft temperature sensor fault	6

Top downtime events of the month (SCADA event log, reviewed with Highline Wind Services).

4. Maintenance

- 17 corrective work orders closed, 5 still open at month end.
- Service lift six-monthly LOLER examinations completed on schedule.

5. Health, safety and environment

Indicator	Month
Hours worked on site (Highline + Weyland)	2,774
Lost time injuries	0
First aid cases	0
Near misses reported	0
Safety observations	14
Environmental incidents	0

No complaints from neighbours were received this month.

6. Outlook

The P50 budget for next month assumes normal seasonal wind; no planned outages beyond routine maintenance.

Prepared by Sara Lindgren (Performance Analyst); reviewed by Ben Okoye (Site Manager) and David Chen (Asset Operations Manager).
