

Monthly Performance Report – August 2024

Kestrel Ridge Wind Farm (75.6 MW)

David Chen · 09 September 2024 · KR-OPS-RPT-2024-08


1. Summary

Kestrel Ridge generated **13.6 GWh** in August 2024, 7.9 % above the P50 budget of 12.6 GWh. Availability of **97.2 %** met the contract target of 97.0 %. Mean hub-height wind speed was 7.2 m/s, above the long-term monthly mean of 6.9 m/s.

2. Production and key figures

KPI	August 2024	Budget / target	YTD 2024	YTD budget
Net generation (GWh)	13.6	12.6	64.9	65.5
Time-based availability	97.2 %	97.0 %	96.2 %	97.0 %
Capacity factor	24.2 %	22.4 %	23.4 %	–
Mean wind speed at hub height (m/s)	7.2	6.9	–	–

Source: Kestrel Ridge SCADA, revenue meter at 132 kV point of connection. Budget = P50 (2024 post-construction yield assessment).

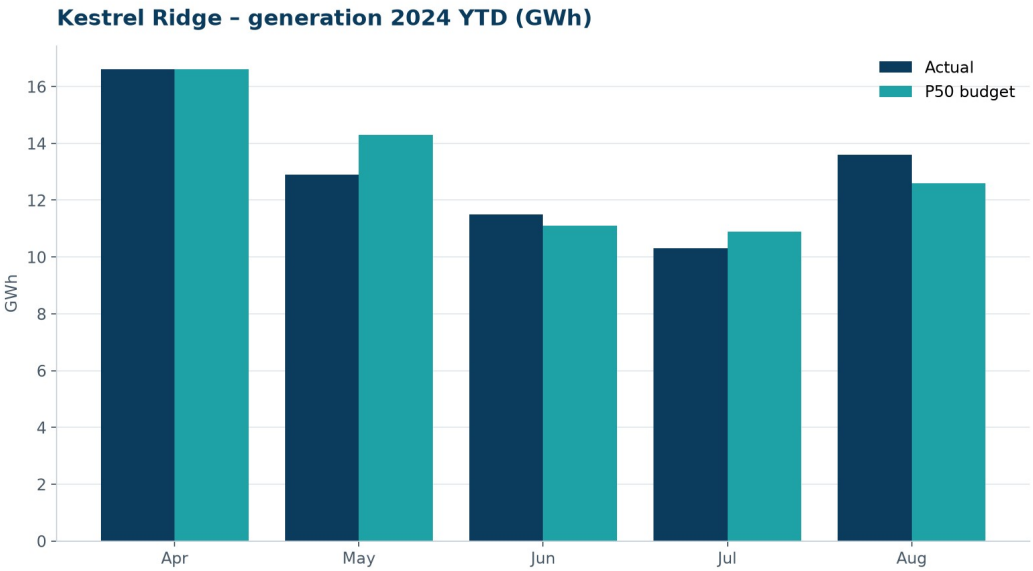

Monthly generation vs. P50 budget, 2024 year to date

3. Availability and downtime

Total turbine downtime attributable to the contractor amounted to 22 turbine-hours for the top events listed below. No grid or force majeure exclusions were claimed this month.

Turbine	Event	Downtime (h)
T-06	hydraulic oil leak at rotor brake caliper	9

T-09	anemometer heater failure – sensor replaced	8
T-06	generator slip ring brush wear alarm	5

Top downtime events of the month (SCADA event log, reviewed with Highline Wind Services).

4. Maintenance

- 14 corrective work orders closed, 5 still open at month end.
- Monthly safety equipment checks (fall arrest, rescue kits, fire extinguishers) completed on all towers.

5. Health, safety and environment

Indicator	Month
Hours worked on site (Highline + Weyland)	2,481
Lost time injuries	0
First aid cases	1
Near misses reported	1
Safety observations	7
Environmental incidents	0

No complaints from neighbours were received this month.

6. Outlook

Next month's focus: closing open corrective work orders and preparing the quarterly O&M review with Highline Wind Services.

Prepared by Sara Lindgren (Performance Analyst); reviewed by Ben Okoye (Site Manager) and David Chen (Asset Operations Manager).
