

Quarterly Construction Report Q2 2026

Harrow Bay Offshore Wind · for Hanseatic Infrastructure Bank and the lender group

Marcus Bell · 15 July 2026 · HB-FIN-LR-2026-Q2

1. Executive summary


Offshore construction started on 7 April 2026. By 30 June, 10 of 40 monopiles and 9 transition pieces were installed, against 12 in the baseline. The offshore substation jacket was installed on 27 June. No lost time injuries; one high-potential near miss (HSE-INC-2026-018) was investigated and closed.

2. Construction progress

Workstream	Status
Foundations	10/40 monopiles installed
Offshore substation	Jacket installed
Export cables	Manufacturing
Turbines	Manufacturing started in Aarhus
Onshore substation	Civil works 40 %

3. Cost and financing

Actual spend to 30 June 2026: EUR 612.0 m. EAC unchanged at EUR 1,620 m; contingency remaining EUR 46.4 m.

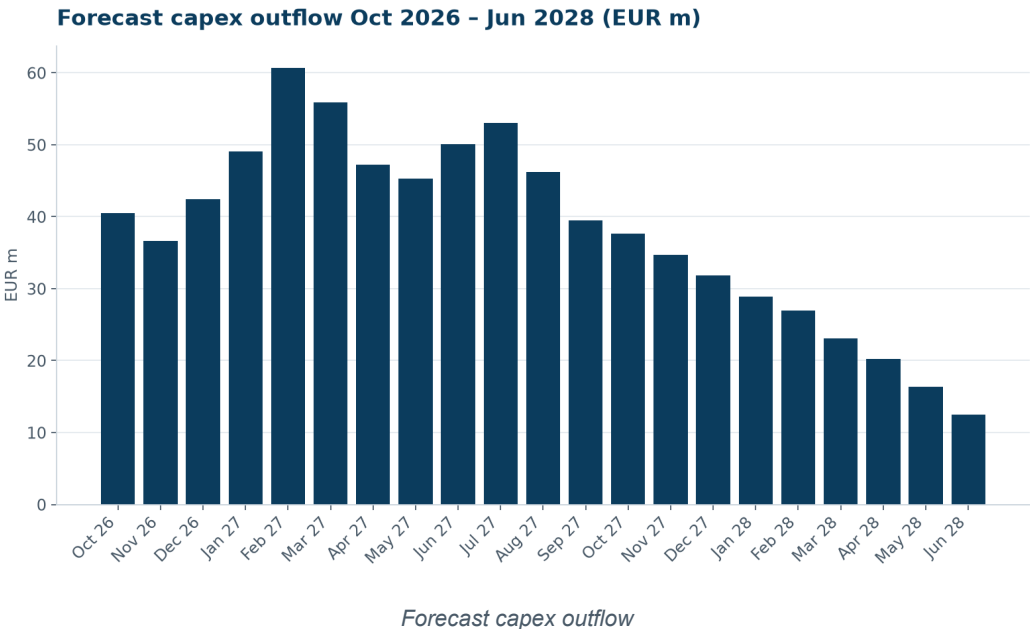

Drawdown	Date	Amount (EUR m)
DR-03	15 Apr 2026	88.4
DR-04	15 May 2026	61.2
DR-05	15 Jun 2026	54.7

4. Key risks

ID	Risk	Rating	Mitigation
HB-RISK-001	Weather	Medium	Weather-window planning
HB-RISK-009	Dropped objects	Medium	DROPS programme strengthened after HSE-INC-2026-018
HB-RISK-004	Turbine delivery	Medium	Production reviews at Halden

5. HSE and environment

Zero lost time injuries. Noise monitoring: one exceedance at HB-A04 (April), all other piles compliant. Marine mammal and seabird monitoring by Marlow Ecology in line with consent conditions.

6. Compliance with finance documents

No event of default. All information undertakings met. The Lenders' Technical Adviser visited the Port of Eastholm and MV Sea Atlas on 19 May 2026.
